


PAMMAL MUNICIPALITY WSS

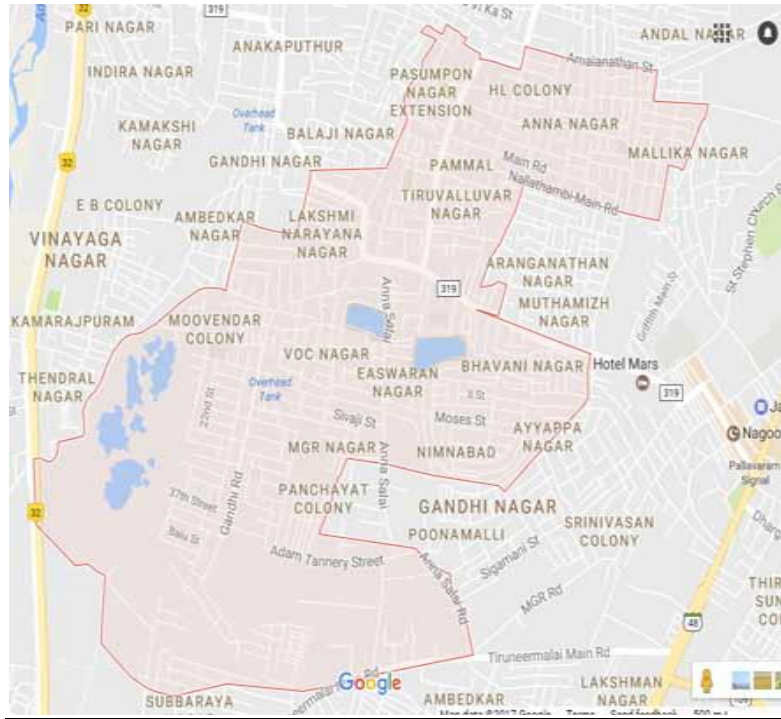

- Pammal Municipality is the recently upgraded third grade municipality in Kanchipuram District and located at 25 KM from Chennai. The Municipality has an extent of 13.81 sqkm and consists of about 877 streets with the total length of about 111 km.
- The population to be benefited by implementing the scheme are 80178,124914 and 194612 in the years 2014, 2029 and 2044 respectively at the rate of 12.43MLD, 19.36 MLD and 30.06 MLD in the corresponding years.
- The scheme cost for providing water supply improvement scheme to Pammal is Rs.4310 Lakhs. The funding pattern for this work TNUDP III 2012-2013 and loan from TNUDP III Rs.2586 lakhs, grant from TNUDP III Rs .1293 lakhs ,ULB contribution Rs.431 Lakhs respectively.
- The Govt.in its G.O Ms.No. 12 MA&WS dept dated 28.01.2013 has accorded administrative approved for this project.

➤ **The Components of Work:**

1. Laying of DI distribution mains of sizes from 100mm to 600mm dia for length of 111872m.
2. Laying of conveying main and feeder main of 150mm to 600mm dia for the length of 6974 m
3. Construction of OHT(4nos)
 - 1.13LL -2nos
 - 2.15LL -1no
 - 3.20LL – 1no
4. Providing House Service Connections for 17093 nos.

➤ **Contract details:**

The work has been awarded to M/s M/s. Shriram Epc Ltd, Chennai at a contract value of Rs.4539Lakhs on 23.09.2013 with a contract period of 18 months and The work was commenced on 31.10.2013.Schedule date of completion was 30.04.2015.

➤ **Progress of work (as on 31.05.2017)**

1. Physical progress – 77.99%
2. Financial – 73.18%
3. Probable date of completion 28.02.2018
